

Florida **PALM**

Planning, Accounting, and Ledger Management



EXECUTIVE STEERING COMMITTEE

DEPARTMENT OF FINANCIAL SERVICES

AUGUST 25, 2021



PROJECT UPDATE

SEAN BUCHANAN, MATTHEW CHRISTOVICH,
SCOTT FENNELL, SHELLEY McCABE, MELISSA TURNER



Florida PALM Project Update

Contract Management

- ▶ Amendment 6 update
 - Deliverable Updates:
 - Central Deliverables merging into Departmental Deliverables
 - Payroll Deliverables are being retained
 - Some Deliverables may be paid based on completion percentage
 - Repeating Deliverables will be moved to the Operational Calendar
 - Future Strategy Deliverables are not needed if not changing
 - Documents will be shared as they are ready for ESC review
 - Contract Amendment, Attachment 1 – Statement of Work, Attachment 2 – Payment Schedule, Attachment 5.1 – Business Requirements, Attachment 6 – Definitions, Attachment 8 – Deliverable Acceptance Criteria, Attachment 10 – Service Level Agreement, Attachment 15 – Optional Services
- ▶ Agency Input on Payroll Timing



Florida PALM Project Update

Contract Management

- ▶ Project Management Plan updates
- ▶ Contract Performance Update
 - Service Level Agreement defines 31 Critical Performance Indicators (CPIs)
 - 23 CPIs activated in July with CMS Wave launch
 - A number of CPIs have a validation period
 - Monthly Performance Report
 - Documents results of all 31 CPIs and includes supporting detail
 - Department confirms metrics and supporting details
 - Highlights for July 2021 results
 - 3 Deliverables submitted on time
 - Production was available for 100% of the 588 hours planned uptime
 - All (406) batch processes completed on time
 - Source code was delivered on time
 - 3.8 average rating for quality of services to Project Team
 - 4.5 average rating for responsiveness to requests of legacy system owners/stakeholders



Florida PALM Project Update

Risks and Issues

- ▶ Since the last ESC meeting, no new issues were logged
- ▶ Since the last ESC meeting, one new risk was logged, three risks remain:
 - 261 – Without an executed contract amendment to define the 2024 implementation approach, the Project implementation and agency adoption schedules are at risk
 - 262 – Agencies may encounter delays in funding releases for transition activities
 - 265 – There may be a misalignment of stakeholder expectations with Project team activities
 - 266 – Unfunded financial resources at agencies may impact Florida PALM transitions
- ▶ Risks and Issues with a high probability and impact will continue to be shared via monthly status reports and discussed (if necessary or as requested) with the ESC



Florida PALM Project Update

Budget – Fiscal Year 21-22


FY 2021-2022 Spend Plan Summary As of July 31, 2021				
Category	Projected FYTD	Incurred FYTD	Released FYTD	Release Remaining
Special Category	\$7,164,232	\$347,932	\$2,000,000	\$1,652,068
SSI Services	\$3,159,655	\$229,457		
Software and Maintenance	\$3,750,335	\$0		
Project Admin	\$75,482	\$6,178		
ERP Support Services	\$76,840	\$52,552		
IV&V	\$101,920	\$59,745		
Contract Contingency	\$0	\$0	\$0	\$0
Salaries and Benefits	\$463,326	\$489,442	\$6,197,071	\$5,707,629
DMS Transfer and Risk Mgmt	\$13,080	\$0	\$25,220	\$25,220
Total	\$7,640,638	\$837,374	\$8,222,291	N/A




At a Glance




Form Metrics (Cumulative)

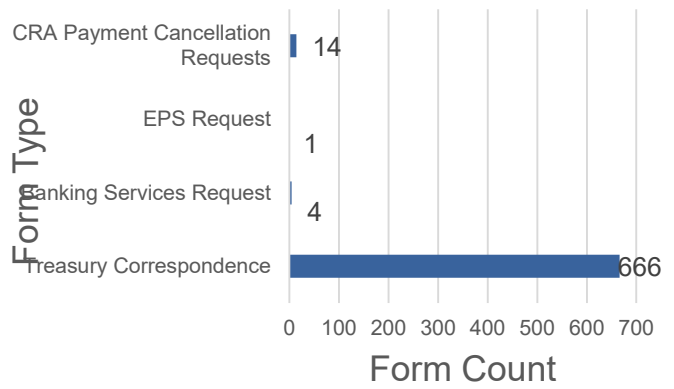

% of Transactions Reconciled

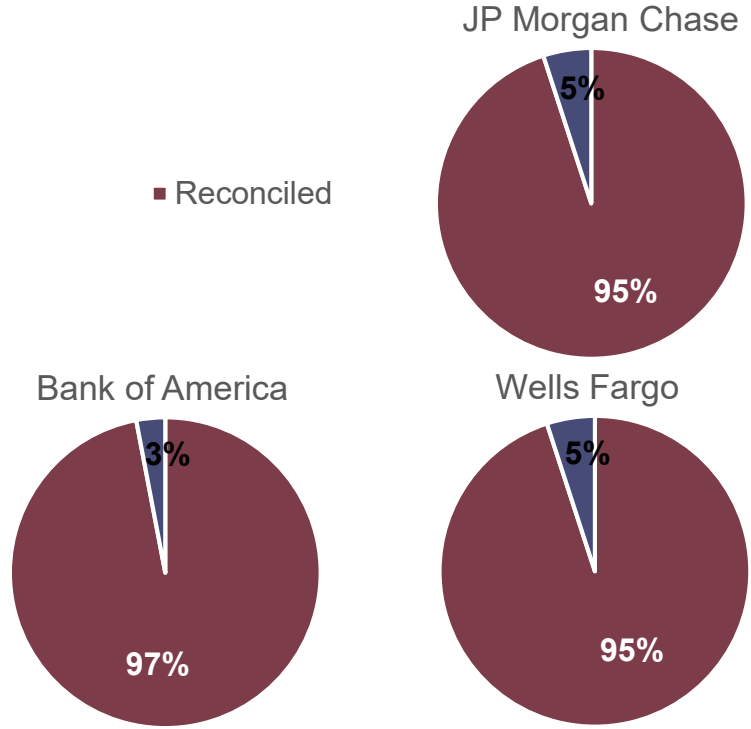


Transaction Metrics

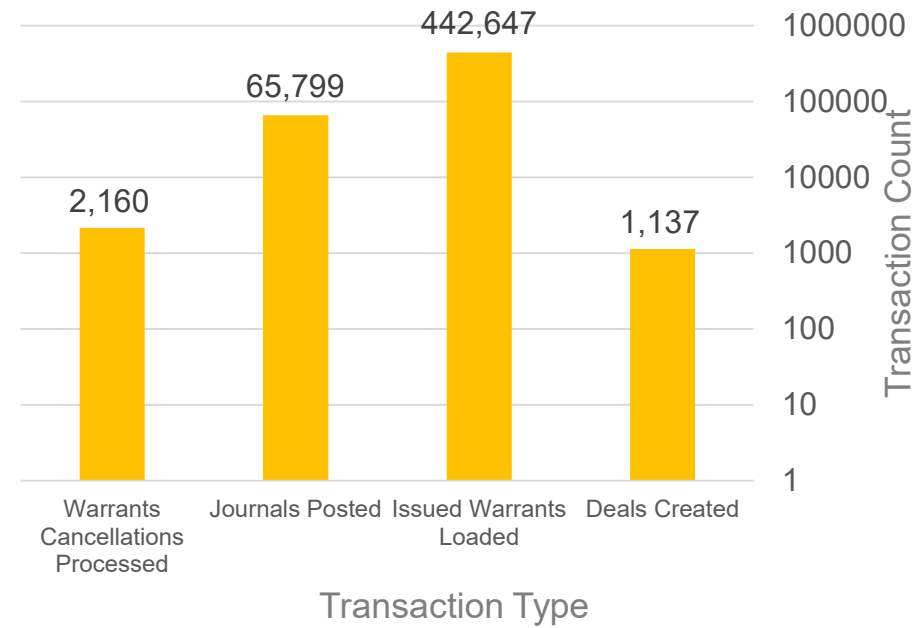

Key Updates

- Processed over \$3,500,000,000 in deposits for DOR
- Preparing for interest apportionment functionality
- Completed July production maintenance (operating system patching)
- Top 3 Incident Categories account for over 62% of all tickets and is a sign end users are actively using Florida PALM
 - "How To" questions
 - Access issues
 - Configuration

Solution Center Incidents

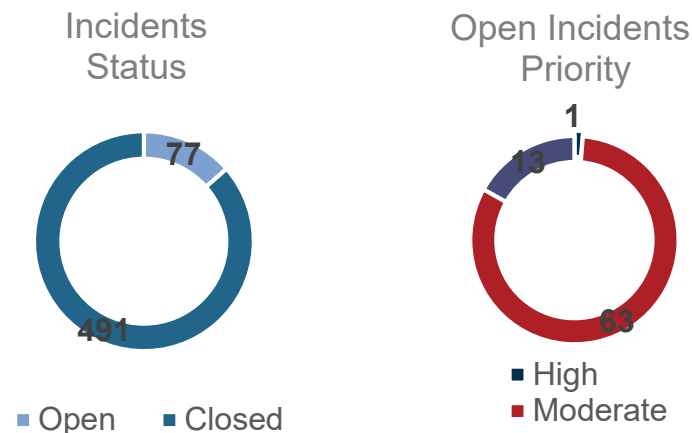

10
Total # of New Incidents Created (8/20)

Florida PALM Project Update

Financial Wave

- ▶ Modules Workgroups
 - New engagement with agencies to understand Florida PALM Modules
 - Kickoff will be held August 31
 - Workgroup sessions will be held this Fall
 - Agency communication to introduce business transformation
- ▶ Interface and Conversion layouts for the Financials Wave
 - 10 conversion layouts shared on 7/30
 - 48 interface layouts shared during CMS and Central Wave activities
 - 21 interface layouts shared on 7/30
 - 10 interface layouts will be shared on 8/30



Florida PALM Project Update



Agency Readiness – Department of Children and Families

- ▶ Fully adopting Florida PALM's capabilities is the least risky, highest-value approach we can take. Combining the Central and Departmental Waves presents the fewest unknowns and best path to success for the project.
- ▶ Risk Management is identifying, assessing, and planning responses to uncertain conditions. Responses include:
 - Avoidance/Exploitation
 - Transfer
 - Mitigate/Enhance
 - Accept



Florida PALM Project Update



Agency Readiness – Department of Children and Families

- ▶ PeopleSoft 9.2 is a fully-mature Enterprise Resource Planning (ERP) system with thousands of enterprise users globally.
- ▶ Florida PALM purchased all but one PeopleSoft modules as an enterprise license; ensuring maximum functionality and complete flexibility on a proven platform.
- ▶ Instead of several standalone databases with an endless inventory of disconnected spreadsheets, ERP systems can create, store, and use the same data derived through common processes.
- ▶ DCF has not found a single business use-case that PeopleSoft is not capable of accomplishing, given sufficient analysis and discussion.



Florida PALM Project Update



Agency Readiness – Department of Children and Families

Florida PALM Project

- ▶ Deliver a working system which can accomplish every business function of CMS and FLAIR.
- ▶ Train the State in how to use system capabilities.
- ▶ Support the analysis of Agency-specific process by fostering dialogue and providing expert guidance on planned Florida PALM functionality

Department of Children and Families

- ▶ Determine how best to use the Florida PALM system to meet our individual mission and business needs.
- ▶ Design agency-specific process information to conform to applicable governance.
- ▶ Train end-users on agency-specific information and duties at each process step.



Florida PALM Project Update

Agency Readiness and Training

- ▶ User Support Labs
- ▶ Tuesday Task Talks
- ▶ Agency communications



INDEPENDENT VALIDATION AND VERIFICATION (IV&V)

CONTENT PROVIDED BY MARK FAIRBANK



IV&V Update

Observations

Florida PALM system production operations are stable and processing most CMS Wave business without disruption

- ▶ Incidents affecting routine automated processing are concentrated in the areas of newly detailed investment accounting and interest apportionment
 - In both areas the Project and Treasury relied on extemporaneous analysis of data scenarios to guide configuration and development rather than having complete requirements and specifications prior to build
 - Incidents that occur as new data is introduced will require remediation
 - Hypercare sessions are productive but consume time and resources
 - Manual contingency processes do not appear sustainable long-term
- ▶ The Production Support incident management process is orderly and draws on Project resources as needed to expedite resolution
- ▶ The frequency and volume of incidents is not extraordinary



IV&V Update

Observations

- ▶ **The deliberations and development of Contract Amendment 6 continue to be productive**
- ▶ While the pace of drafting the amendment is faster than prior amendments, it still appears the effort will take many weeks to complete
- ▶ The Project team has identified work that should proceed immediately because its definition and form are not affected by the shift in approach
- ▶ To avoid loss of the benefit of time gained by the Financials Wave Decision, a speedy finalized Amendment 6 is essential to provide definitive direction and schedule to Enterprise Partners and Agencies



IV&V Update

Observations

Risk of Reliance on Crosswalks and Ongoing Data Translation

- ▶ With the decision to consolidate Central & Departmental Waves into a single Financials Wave, the need to translate FLAIR-to-Florida PALM and vice versa on a daily basis is greatly reduced
- ▶ The Project does not plan to extend and maintain data crosswalks beyond implementation
- ▶ However, the idea of translating data to avoid the need to modify legacy systems has gained popularity
- ▶ If organizations invest in crosswalk programs that enable legacy systems to continue to operate using FLAIR data elements, there are immediate risks to implementation quality and long-term risks to business continuity once FLAIR data maintenance ceases and Florida PALM data evolves



UPCOMING

MELISSA TURNER



Florida PALM Project Update

Upcoming

- ▶ Recommendation of Statutory Changes in November
- ▶ Request for suggested future ESC meeting topics



NEXT SCHEDULED MEETING

SEPTEMBER 22, 2021

LOCATION TBA



CONTACT INFORMATION

FLORIDAPALM@MYFLORIDACFO.COM

MYFLORIDACFO.COM/FLORIDAPALM

